DEVELOPMENT METHODOLOGY


The Course Academy (LMS) project follows the Agile Development Methodology.
Methodology Justification

- Iterative Development: Develop and test the system in small increments.
- Flexibility: Adapt to changing requirements and user feedback.
- Collaboration: Improve teamwork and track project progress.
- Early Risk Detection: Identify and resolve issues throughout development.


TIME ESTIMATION

Symbol	Task	Duration	Depends On
A	Define Project Goals	1 day	—
B	Define Project Scope and Resources	1 day	A
C	Gather System Requirements	2 days	B
D	Define Functional Requirements	2 days	C
E	Design User Interfaces (UI)	2 days	D
F	Design Database	2 days	D
G	Develop User Management	3 days	E, F
H	Develop Courses and Enrollment	4 days	G
I	Test System and Prepare Final Submission	2 days	H

Pert Chart

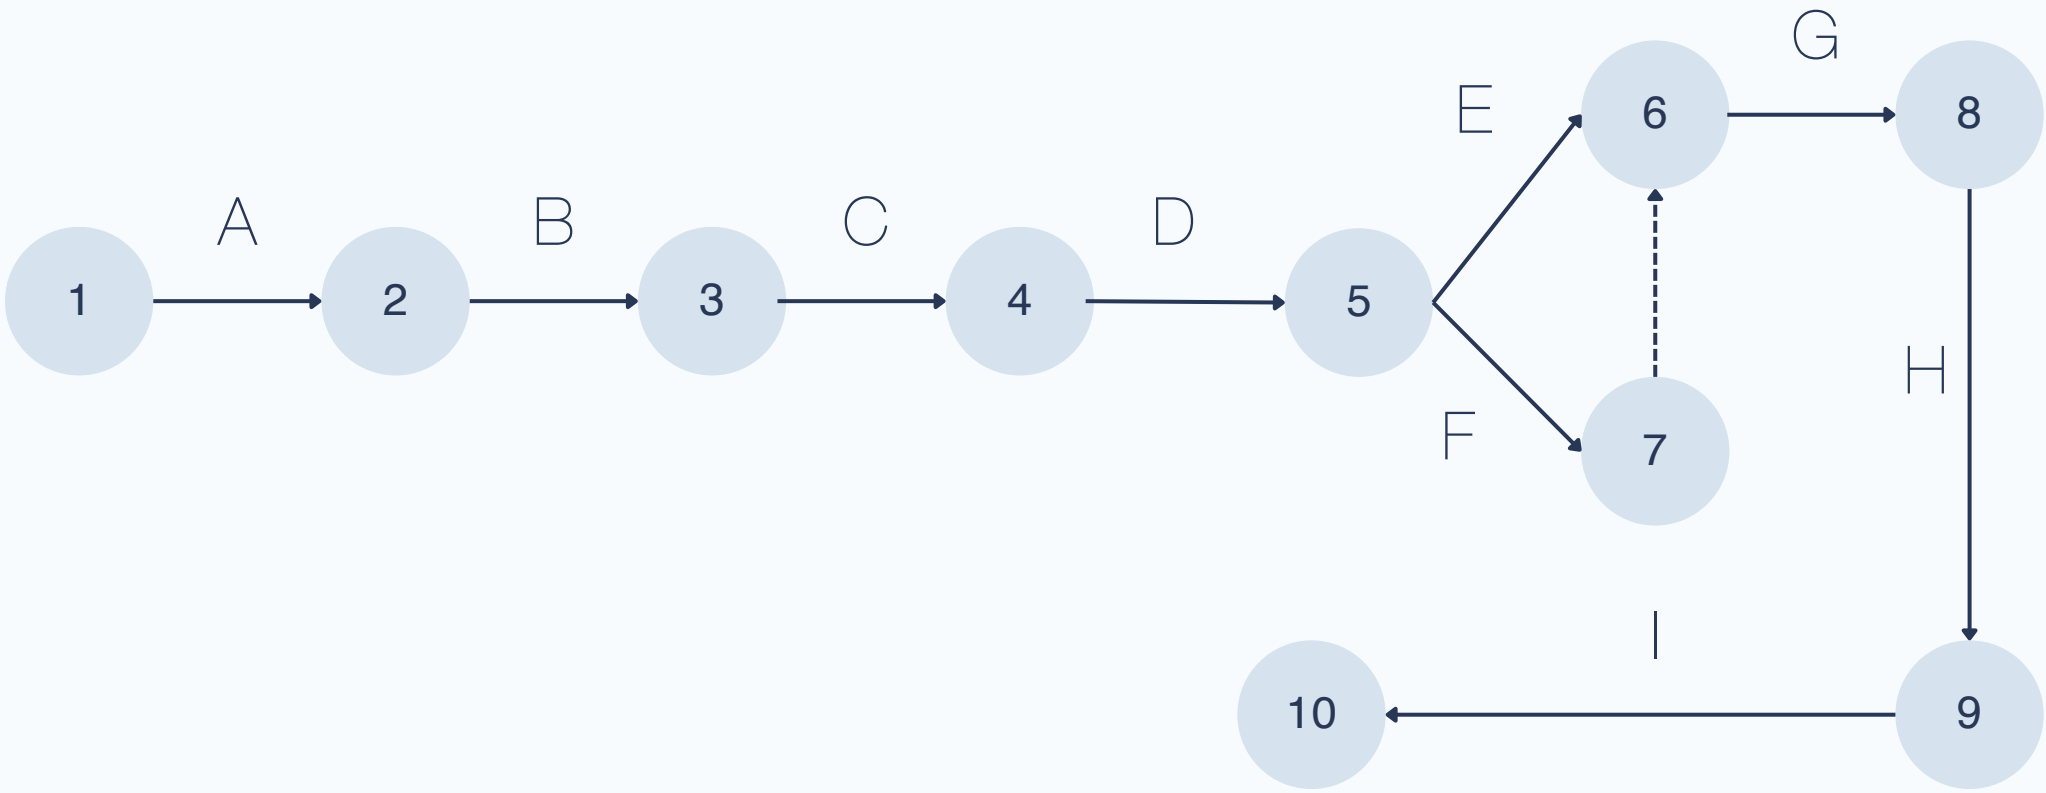

Gantt Chart

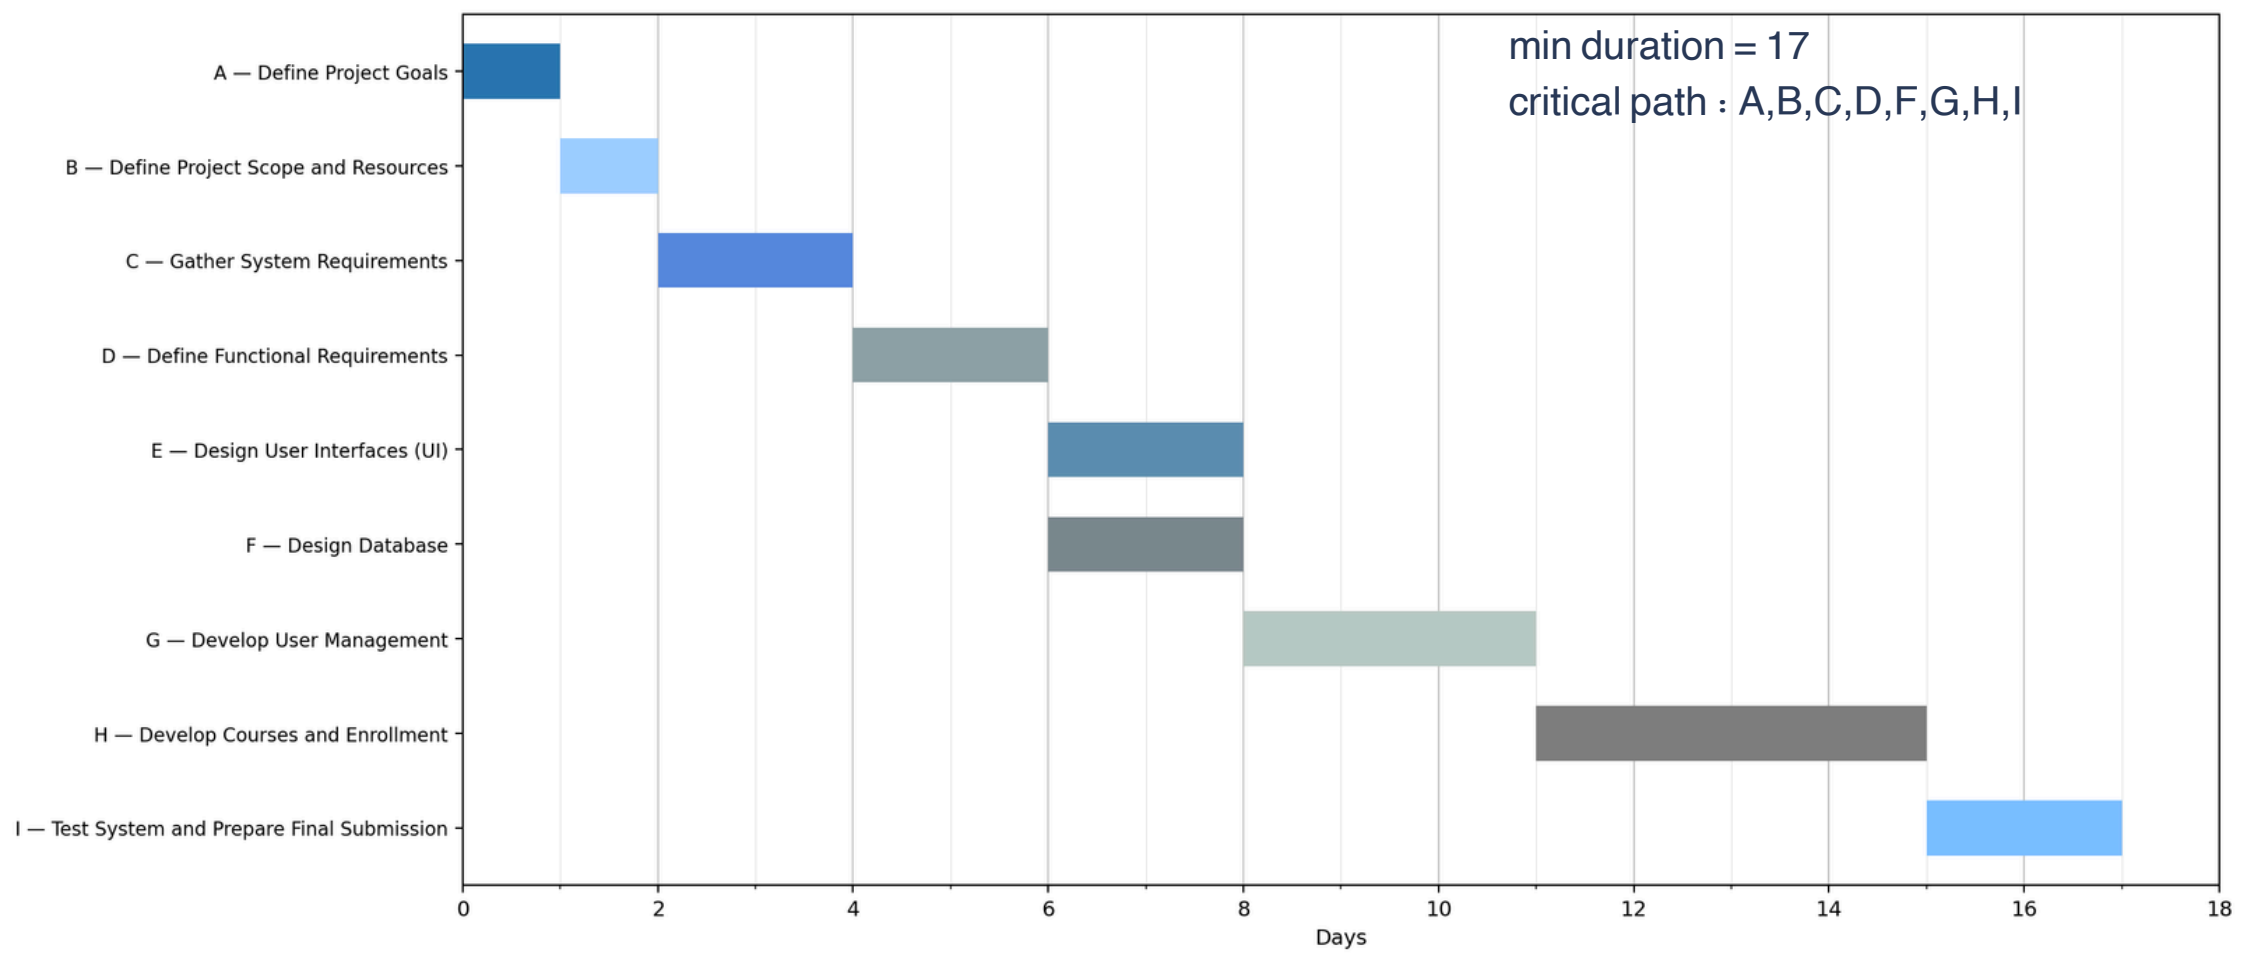
min duration = 17
critical path : A,B,C,D,F,G,H,I
A — Define Project Goals
B — Define Project Scope and Resources
C — Gather System Requirements
D — Define Functional Requirements
E — Design User Interfaces (UI)
F — Design Database
G — Develop User Management
H — Develop Courses and Enrollment
I — Test System and Prepare Final Submission
0
2
4
6
8
10
12
14
16
18
Days
